


Actual Work    ◆ Milestone  
 Remaining Work

Activity ID	Activity Name	Original Duration	Start	Finish	March 2010					April 2010	
					28	07	14	21	28	04	
<b>GULCH GRADING &amp; RIP RAP PLACEMENT</b>											
<b>EARTHWORK</b>											
EXEC0150	Environmental Clearance Knox to Federal 1567+25 to 1!	35	03-Mar-10	20-Apr-10	[Green Bar]						
EXEC0230	Fine Grade Bikepath Between Sheridan and Perry	3	30-Mar-10	01-Apr-10							[Green Bar] Fine Grade Bikepath Between
EXEC0200	Grade Guideway - DGW to DGE (includes remaining ex	7	02-Apr-10	12-Apr-10							[Green Bar]
EXEC0240	Install Bikepath Between Sheridan and Perry	10	02-Apr-10	15-Apr-10							[Green Bar]
<b>UTILITIES</b>											
UTIL0050	XCEL - Gulch - Reset Light Poles 1515+95 to 1539+05	5	02-Apr-10	08-Apr-10							[Green Bar] XC
<b>DROP STRUCTURE #3</b>											
<b>EARTHWORK</b>											
DROP0150	Mass Ex & Subgrade Stabilization for DS-3	5	04-Feb-10 A	26-Feb-10 A	[Blue Bar]	Mass Ex & Subgrade Stabilization for DS-3					
DROP0050	DS-3 Cutoff Wall (All)	3	03-Mar-10	05-Mar-10							[Green Bar] DS-3 Cutoff Wall (All)
DROP0060	DS-3 36 Boulder Placement	13	03-Mar-10	19-Mar-10							[Green Bar] DS-3 36 Boulder Placement
DROP0070	DS-3 Grout Placement	1	22-Mar-10	22-Mar-10							[Green Bar] DS-3 Grout Placement
DROP0160	Ex and Install Rip Rap West of DS-3	5	23-Mar-10	29-Mar-10							[Green Bar] Ex and Install Rip Rap West of DS-3
<b>WALLS</b>											
<b>CONSTRUCT WALL - D-15 - 1552+59 to 1563+84</b>											
<b>WALLS</b>											
350	OCS Foundation 1552+80 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1552+80 F, R, P, & S
360	OCS Foundation 1553+60 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1553+60 F, R, P, & S
370	OCS Foundation 1554+40 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1554+40 F, R, P, & S
380	OCS Foundation 1555+20 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1555+20 F, R, P, & S
390	OCS Foundation 1556+00 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1556+00 F, R, P, & S
400	OCS Foundation 1557+20 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1557+20 F, R, P, & S
410	OCS Foundation 1558+00 F, R, P, & S	6	03-Mar-10	10-Mar-10							[Green Bar] OCS Foundation 1558+00 F, R, P, & S
<b>EARTHWORK</b>											
480	Backfill D-15 Final Grade 1552+60 to 1561+25	7	11-Mar-10	19-Mar-10							[Green Bar] Backfill D-15 Final Grade 1552+60 to 1561+25
<b>CONSTRUCT WALL - D-61 -</b>											
<b>WALLS</b>											
WALL8270	Wall D61 Shop Drawing Approval by RTD, COD	15	10-Feb-10 A	05-Mar-10	[Blue Bar]	Wall D61 Shop Drawing Approval by RTD, COD					
WALL8430	Existing Timberwall demolition, Tree removal	2	08-Mar-10	09-Mar-10							[Green Bar] Existing Timberwall demolition, Tree removal
WALL8280	Wall D61 Construction	5	10-Mar-10	16-Mar-10							[Green Bar] Wall D61 Construction
<b>STREET RECONSTRUCTION</b>											
<b>CONSTRUCT 12th AVE.</b>											
<b>ROADWAY/FLATWORK</b>											
12TH0110	Pavement (1 lift SX100) - 1546+50 to 1552+75	0	05-Apr-10*	05-Apr-10							[Green Bar] Pavement (1 lift
<b>CONSTRUCT KNOX CT.</b>											
<b>ROADWAY/FLATWORK</b>											
KNOX1000	Demo Knox Court (all remaining features)	2	12-Feb-10 A	26-Feb-10 A	[Blue Bar]	Demo Knox Court (all remaining features)					
KNOX1070	Finish Ex W. Side and Prep and Place Fills	4	24-Feb-10 A	27-Feb-10 A	[Blue Bar]	Finish Ex W. Side and Prep and Place Fills					
KNOX1010	Fine Grade for Sidewalks, C&G, and Bus Bay West Side	1	27-Feb-10 A	01-Mar-10 A	[Blue Bar]	Fine Grade for Sidewalks, C&G, and Bus Bay West Side					
KNOX1120	F/P/S West side sidewalkds, C&G, Bust Bay	4	02-Mar-10 A	04-Mar-10							[Green Bar] F/P/S West side sidewalkds, C&G, Bust Bay
KNOX1170	Snow Removal and Frost Ex East Side	1	05-Mar-10	05-Mar-10							[Green Bar] Snow Removal and Frost Ex East Side
KNOX1180	Frost ex and Start Fills East Side	1	08-Mar-10	08-Mar-10							[Green Bar] Frost ex and Start Fills East Side
KNOX1190	Finalize Fills and Compact East Side	1	09-Mar-10	09-Mar-10							[Green Bar] Finalize Fills and Compact East Side

[Blue Bar] Actual Work    ◆ Milestone  
 [Green Bar] Remaining Work

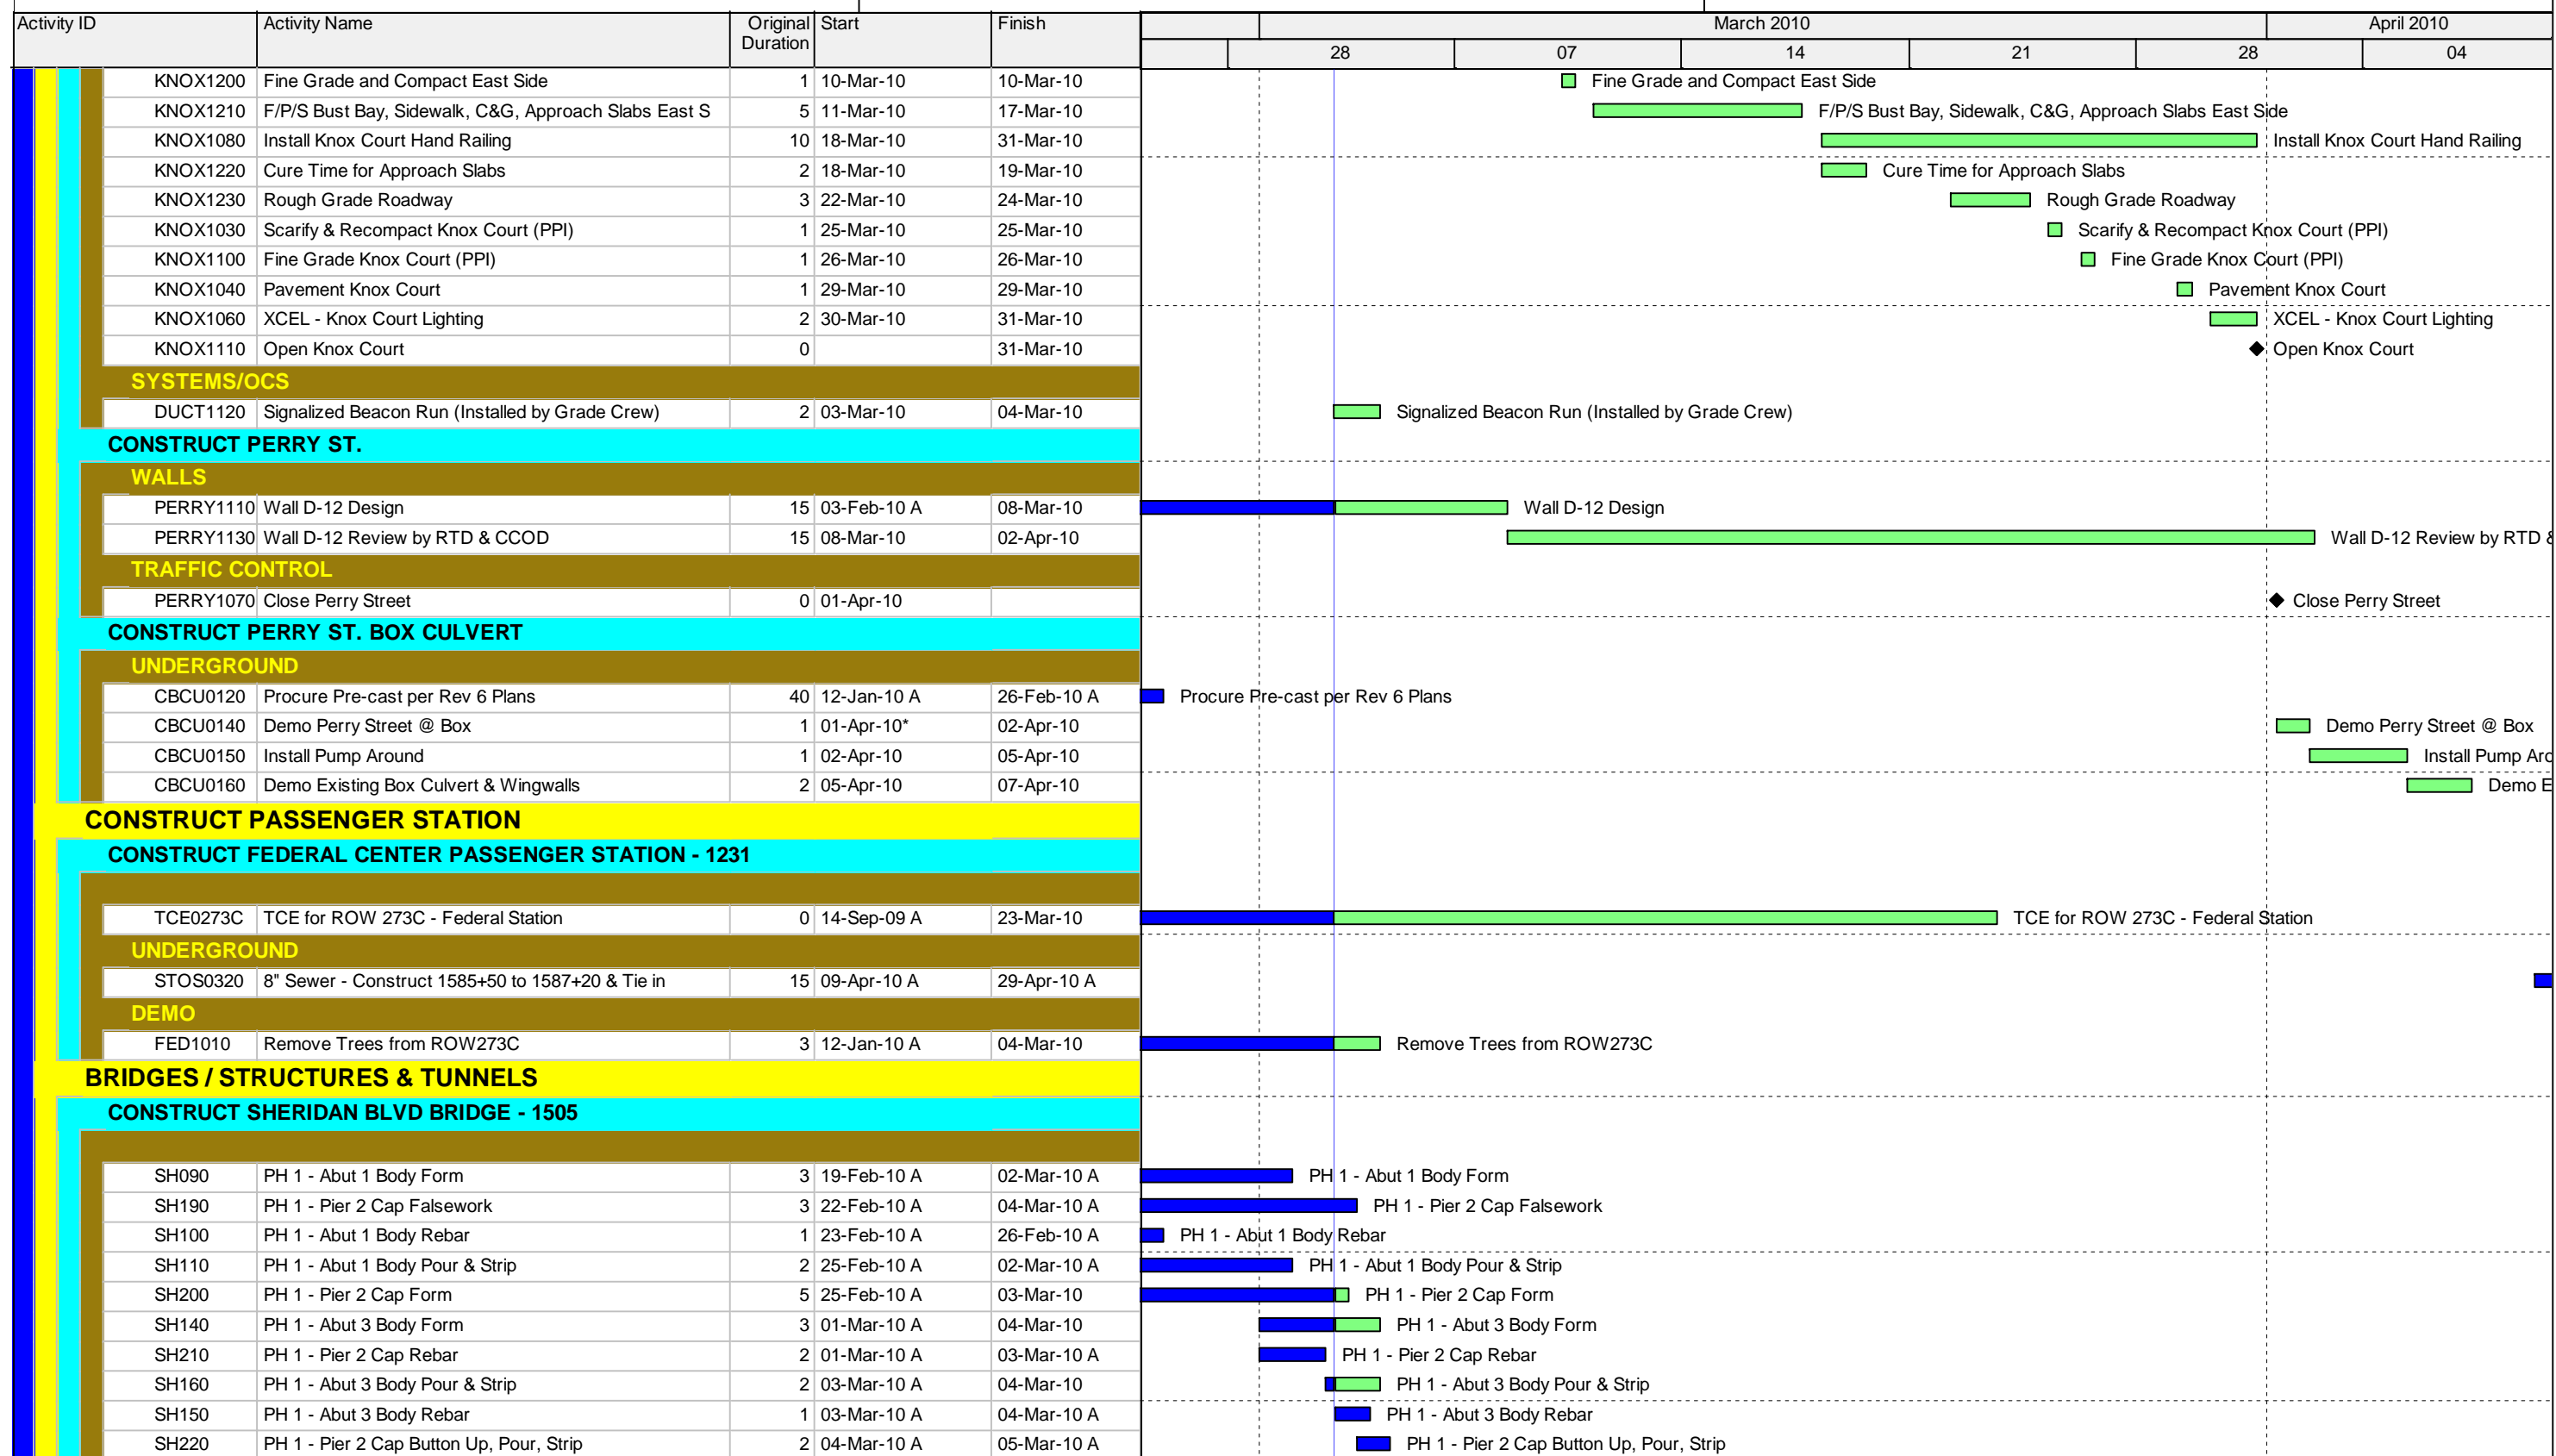

Actual Work    ◆ Milestone  
 Remaining Work

Activity ID	Activity Name	Original Duration	Start	Finish	March 2010					April 2010	
					28	07	14	21	28	04	
SH230	PH 1 - Erect Girders	3	08-Mar-10 A	08-Mar-10							
SH240	PH 1 - Form Deck & Diaphragms	20	08-Mar-10	12-Apr-10							
SH250	PH 1 - Install Waterline Casing	10	08-Mar-10	25-Mar-10							
SH245	PH 1 - Deck Rebar	5	06-Apr-10	14-Apr-10							
<b>DEMO</b>											
BRDG0980	Sheridan South Structure Demo	36	02-Feb-10 A	08-Mar-10							
BRDG0960	Sheridan North (2nd grp) Disconnects, Abatement prog	30	26-Mar-10*	06-May-10							
<b>CONSTRUCT TENNYSON PED BRIDGE - 1535</b>											
<b>BRIDGE</b>											
BRDG2220	Mount Poles (Xcel)	3	08-Mar-10	10-Mar-10*							
<b>ROADWAY/FLATWORK</b>											
BRDG1930	Tennyson South Abut Sidewalk and Stairs 1535	7	11-Mar-10	19-Mar-10							
BRDG1940	Tennyson North Abut Sidewalk - 1535	3	22-Mar-10	24-Mar-10							
<b>CONSTRUCT HAZEL CT. BRIDGE - 1579</b>											
<b>BRIDGE</b>											
BRDG1820	Mount Poles (Xcel)	3	02-Mar-10 A	05-Mar-10							
<b>ROADWAY/FLATWORK</b>											
KNOX1150	Grade Hazel Court Approaches	1	03-Mar-10	03-Mar-10							
KNOX1160	Pave Hazel Court Approaches	1	04-Mar-10	04-Mar-10							
BRDG1710	Hazel Court South Abut Sidewalk	3	08-Mar-10	10-Mar-10							
BRDG1720	Hazel Court North Abut Sidewalk	4	11-Mar-10	16-Mar-10							
<b>CONSTRUCT FEDERAL BLVD BRIDGE - 1590</b>											
ROW0281	ROW 281	0	26-Mar-10*								
ROW0282	ROW 282	0	26-Mar-10*								
<b>BRIDGE</b>											
FE190	Federal Bridge	210	22-Jun-09 A	20-Jan-11							
FE290	PH 1C - Remove Portion of Bridge	4	03-Mar-10	09-Mar-10							
FE380	Federal PH 1C Substructure	23	03-Mar-10	13-Apr-10							
FE300	PH 1C - Pier 2 Caissons - 1ea - 42	1	10-Mar-10	11-Mar-10							
FE310	PH 1C - Pier 2 Column 1 Rebar, Form, Pour, & Str	3	11-Mar-10	16-Mar-10							
FE320	PH 1C - Pier 3 Caissons - 1ea - 42	1	11-Mar-10	12-Mar-10							
FE340	PH 1C - Abut 4 Caissons - 7ea - 36	2	12-Mar-10	16-Mar-10							
FE350	PH 1C - Pier 3 Column 1 Rebar, Form, Pour, & Str	3	12-Mar-10	18-Mar-10							
FE360	PH 1C - Pier 2 Cap Falsework	2	17-Mar-10	19-Mar-10							
FE370	PH 1C - Abut 1 Caissons - 2ea - 24	1	17-Mar-10	18-Mar-10							
FE410	PH 1C - Abut 4 Body Form & Rebar	2	17-Mar-10	19-Mar-10							
FE400	PH 1C - Pier 3 Cap Falsework	2	18-Mar-10	22-Mar-10							
FE390	PH 1C - Pier 2 Cap Form & Rebar	2	19-Mar-10	23-Mar-10							
FE430	PH 1C - Abut 4 Body Button Up, Pour, & Strip	2	19-Mar-10	23-Mar-10							
FE420	PH 1C - Pier 2 Cap Button Up, Pour, & Strip	2	24-Mar-10	26-Mar-10							
FE460	PH 1C - Abut 1 Body Form & Rebar	2	24-Mar-10	26-Mar-10							
FE440	PH 1C - Pier 3 Cap Form & Rebar	3	26-Mar-10	01-Apr-10							
FE450	PH 1C - Pier 2 Cap Cure	6	26-Mar-10	02-Apr-10							
FE480	PH 1C - Abut 1 Body Button Up, Pour, & Strip	2	26-Mar-10	30-Mar-10							
FE470	PH 1C - Pier 3 Cap Button Up, Pour, & Strip	2	01-Apr-10	05-Apr-10							

Actual Work ◆ Milestone  
 Remaining Work

Activity ID	Activity Name	Original Duration	Start	Finish	March 2010					April 2010		
					28	07	14	21	28	04		
FE500	PH 1C - Pier 3 Cap Cure	6	05-Apr-10	13-Apr-10								
<b>UNDERGROUND</b>												
UTIL2220	Push Pipe STA 6+74.53-3+69.92	4	03-Mar-10	09-Mar-10								
UTIL2230	Install Expansion Joints/Anchor Rings	2	10-Mar-10	12-Mar-10								
UTIL2240	Install Pipe STA 8+00.00-6+74.53	4	12-Mar-10	19-Mar-10								
UTIL2250	Install Wet Tap 7+56.19 (DWB)	1	19-Mar-10	22-Mar-10								
UTIL2260	Install Access Manhole STA 7+01.59	1	22-Mar-10	23-Mar-10								
UTIL2270	Install 6" Blowoff Manhole STA 6+95.00	2	24-Mar-10	26-Mar-10								
UTIL2290	Install Pipe STA 3+69.92-2+30.00	4	26-Mar-10	02-Apr-10								
UTIL2300	Install Blowoff Manhole STA 3+53.34	2	02-Apr-10	06-Apr-10								
UTIL2280	Construct Expansion Vault STA 6+66.30	8	05-Apr-10*	19-Apr-10								
<b>DEMO</b>												
DEMO1020	Demo Billboard on ROW282 (Security Reality)	2	03-Mar-10	04-Mar-10								
DEMO1010	Demo ROW261 (Bonilla)	5	25-Mar-10*	31-Mar-10								
<b>TRAFFIC CONTROL</b>												
PREC0460	Federal Phase 1 Setup	1	03-Mar-10*	03-Mar-10								
<b>CONSTRUCT DECATUR ST BRIDGE - 1597</b>												
<b>ROADWAY/FLATWORK</b>												
ROW0286	ROW 286, 286A, 286B, & 286C	0	03-Mar-10*									
<b>UTILITIES</b>												
UTIL1820	Qwest Infrastructure 15-64	11	21-Dec-09 A	04-Mar-10								
UTIL1830	Adesta Fiber 18-3	15	03-Mar-10	23-Mar-10								
UTIL1870	Qwest Cut-Over 15-64	25	05-Mar-10	08-Apr-10								
<b>CONSTRUCT LAKEWOOD GULCH BRIDGE - 1600</b>												
<b>BRIDGE</b>												
BRDG1810	Lakewood Gulch Bridge	87	01-Jun-09 A	06-Jul-10								
LA21	LRT Over Lakewood Gulch Superstructure	67	22-Oct-09 A	15-Apr-10								
LA240	Sidewalks	10	22-Mar-10*	07-Apr-10								
<b>CONSTRUCT SOUTH PLATT RIVER BRIDGE - 1608</b>												
<b>BRIDGE</b>												
TCE0273F	TCE from CCOD for Platte properties around ROW 273F	20	30-Oct-09 A	19-Mar-10								
ROW0325	ROW 325 (Seigel)	0	03-Mar-10*									
ROW0325A	ROW 325A (Seigel)	0	03-Mar-10*									
<b>BRIDGE</b>												
11GEN40	Mobilize	4	24-Mar-10*	29-Mar-10								
ROW0343	ROW 343 (West Bank of Platte)	0	30-Mar-10*									
11GEN50	Traffic Control/Bikepath Detour	2	30-Mar-10	31-Mar-10								
11GEN60	Erosion Control	2	01-Apr-10	05-Apr-10								
11DIRT10	Grade Access for Falsework Piling - WEST	3	06-Apr-10	09-Apr-10								
<b>UTILITIES</b>												
UTIL2050	XCEL - Relocate Primaries - S. Platte	20	16-Oct-09 A	23-Mar-10								
<b>CONSTRUCT CML FLYOVER - 1624</b>												
<b>BRIDGE</b>												
BRDG0930	BNSF Access Permit (RTD)	30	02-Nov-09 A	16-Mar-10								
BRDG0950	Pick Plan Development	15	02-Nov-09 A	09-Mar-10								

█ Actual Work    ◆ Milestone  
█ Remaining Work

Activity ID	Activity Name	Original Duration	Start	Finish	March 2010					April 2010	
					28	07	14	21	28	04	
BRDG0990	BNSF Approval of Pick Plan	50	10-Mar-10	18-May-10							
12MOB	Mob/Setup Yard & Access	4	02-Apr-10*	07-Apr-10							
<b>DEMO</b>											
DEMO030	Fill in pit @ 1801 W. 14th St	5	03-Mar-10*	09-Mar-10							
DEMO040	Sewer Lateral Cut & Inspection @ 1801 W. 14th St	2	25-Mar-10	29-Mar-10							
DEMO060	Water Lateral Cut & Inspection @ 1801 W. 14th St	2	29-Mar-10	31-Mar-10							
DEMO050	Sewer Lateral Cut & Inspection @ 2750 W. 14th St.	2	31-Mar-10	02-Apr-10							
DEMO070	Water Lateral Cut & Inspection @ 2750 W. 14th St.	2	02-Apr-10	06-Apr-10							
<b>TRAFFIC CONTROL</b>											
12MOB40	Close Shoshone & 14th Avenue	1	02-Apr-10	02-Apr-10							
<b>BALLAST &amp; TRACK</b>											
<b>BURNHAM YARD LEAD</b>											
<b>UNDERGROUND</b>											
BURN1000	Storm Sewer - Lower Colfax 20+00	8	05-Apr-10*	14-Apr-10							
<b>UTILITIES</b>											
UTIL9030	Remove Telephone Pole 100+20 by Qwest	1	03-Mar-10	03-Mar-10							
UTIL9040	Remove Telephone Pole 104+05 by Xcel	1	03-Mar-10	03-Mar-10							
UTIL9050	Reset Light Pole 105+50 by Xcel	1	03-Mar-10	03-Mar-10							
UTIL9060	Reset Telephone Poles & Guys on Shoshone by Xcel	5	03-Mar-10	09-Mar-10							
UTIL9100	Reset Telephone Poles Rio Ct. by Qwest	1	03-Mar-10	03-Mar-10							
UTIL9110	Reset Telephone Poles Rio Ct. by Xcel	3	03-Mar-10	05-Mar-10							
UTIL9120	Abandon 2" Gas Rio Ct. by Xcel	2	03-Mar-10	04-Mar-10							
UTIL9130	UG Transmission Encasement 13th Ave by Xcel	10	03-Mar-10	16-Mar-10							
UTIL9140	20" Steam Encasement 13th Ave by Xcel	5	03-Mar-10	09-Mar-10							
UTIL9150	Reset Telephone Pole and Cabinet 13th Ave by Xcel	5	03-Mar-10	09-Mar-10							
UTIL9160	Relocate 13th Ave Gate & Signal by UPRR	5	03-Mar-10	09-Mar-10							
<b>DEMO</b>											
DEMO001	Abatement & Disconnects 1800 W. Colfax	60	18-Jan-10 A	07-May-10							
DEMO011	Abatement & Disconnects 1350 Rio Ct	60	18-Jan-10 A	07-May-10							
<b>SIEGEL OIL SPUR</b>											
BATK0080	Siegel SWMP	1	02-Apr-10	05-Apr-10							
<b>TRACK</b>											
BATK0090	Weld Siegel Oil Phase 1 Strings	2	19-Jan-10 A	03-Mar-10							
PREC0120	PUC Permit for Umatilla Crossing	20	26-Feb-10 A	25-Mar-10							
PREC0040	Design Acceptance by Seigel Oil	5	03-Mar-10	09-Mar-10							
BATK0030	Seigel Oil Spur Phase 1	5	26-Mar-10*	01-Apr-10							
BATK0050	Seigel Oil Spur Phase 2	8	02-Apr-10	13-Apr-10							

Actual Work    ◆ Milestone  
 Remaining Work
